Change Management Practitioner Program

Participant Profile

Your responses to the following questions will help your instructor tailor the delivery of the program content to support your learning experience.

1. Name

2. Email

3. What is your current role?

4. How many years of experience do you have in your current role?

- ○ Less than 1 year
- ● 1 – 3 years
- ○ 4 – 5 years
- ○ > 5 years

5. What percentage of your time is/will be focused on change management?

- ● 0% – 25%
- ○ 26% – 50%
- ○ 51% – 75%
- ○ 76% – 100%

6. How do you intend to use the knowledge you will gain from this program in your current role?

© Prosci, Inc. All rights reserved

7. Which one of the following levels most accurately describes your current change management competency?

- ● **Novice** - I have limited experience with change management and adhere to the rules I was taught.
- ○ **Advanced Beginner -** I leverage basic situation perception of change management while treating separate aspects with equal importance.
- ○ **Competent** - I use a standard approach for change management that includes deliberate planning to address multiple activities and information sources, so my actions contribute to goals.
- ○ **Proficient** - I develop a holistic view of the situation and can perceive deviations from the norm while employing guidelines that I adapt to the situation to effectively prioritize my change management efforts.
- ○ **Expert** - I leverage my intuition and deep understanding, informed by a vision of what is possible, to read the situation and move beyond reliance on change management rules or guidelines in order to adapt my work to the situation at hand.

8. What are your learning objectives for the program?

9. Review the following four learning styles and rank them from 1 (my most preferred learning style) to 4 (my least preferred style).

Activist - I want to experience the material (short activities, diversity, challenge and teamwork)	○ 1	○ 2	○ 3	○ 4
Reflector - I want time to reflect on the experience (process activities, listen, observe, think, research, structured exchange of views and no time constraints)	○ 1	○ 2	○ 3	○ 4
Theorist - I want to take time to make conclusions about the material (concepts, theories, methodical approach, clear aims, questioning, intellectual stretching, listening, reading and complexity)	○ 1	○ 2	○ 3	○ 4
Pragmatist - I want to test out and apply what I am learning (Practical issues, relevant information, practice of techniques, link to work situations, immediacy and simplicity)	○ 1	○ 2	○ 3	○ 4

© Prosci, Inc. All rights reserved

Change Management Practitioner Program

Project Selection – Frequently Asked Questions

Why do I need a project for the program?

The Prosci Change Management Practitioner Program uses an applied learning approach. During the program, you will apply the Prosci Methodology to a real project that you are working on as a change practitioner. For example, one of your tasks will be to develop a short presentation on change management to a real audience with a real ask. You will also learn how to use a number of assessment tools by applying them to your project, analyzing the results, and using the new insights you have gained to begin developing the change management approach for your project. You will leave the program with practical deliverables, such as your completed presentation, that you can immediately use and continue to develop post-program.

What makes a good project?

To determine if the project you've selected is a good choice to support your learning in the program, assess it against the following criteria:

- [ ] The benefits are highly dependent on adoption and usage of the change.
- [ ] The project is at an early stage and there is significant opportunity to apply change management to influence the outcomes.
- [ ] The project is of a manageable size and complexity or it is possible to focus on a portion of the overall project.
- [ ] You have knowledge of the reasons your organization has decided to implement the change.
- [ ] You have knowledge of the project details (solution being developed, scope, timeline, etc.)
- [ ] You have knowledge of the project objectives (what the project will achieve).
- [ ] You have knowledge of the organization benefits (what the organization will gain).
- [ ] You have knowledge of the sponsor(s) of the change.
- [ ] You have knowledge of the groups that will be impacted and the types of impacts they will experience.

If you can't place a checkmark against each criterion, review the questions and answers on the following page for additional guidance on how to address any significant gaps.

© Prosci, Inc. All rights reserved

What if the scope of my project is very large?

If the initiative you are working on is actually a program comprised of a number of projects, such as implementing a new IT system in multiple countries over an extended time period, focus on one of the projects for the Practitioner Program (e.g., year one of the implementation in the first country). Given the limited amount of time during the program that is available for application, you will be able to gain a deeper understanding of the methodology by focusing on a portion of the larger initiative.

What if I'm not yet familiar with my project?

Using a project you aren't familiar with during the program will limit your learning, as you won't have enough information to fully complete the assessments. However, there are actions you can take pre-program to learn more about the project and ensure that you have the best possible learning experience. These actions might include:

- Meeting with your project sponsor to get an explanation of why the change is needed and an understanding of the expected benefits of the change for the organization.
- Asking the project manager to describe the solution that is being developed and provide details about who will be impacted, the project timeline, and scope.
- Asking the project manager for project documentation such as a project charter.
- Speaking with managers who are impacted by the change to gain their perspectives on the change and how it will impact their teams.

Use the criteria listed under "What makes a good project?" to identify the specific information you need to collect and from whom prior to the program.

What if I don't have a current project?

If you are in this situation, you can use a past change project that you are very familiar with (see the criteria for what makes a good project above). When using a past project, it can be helpful to imagine that you are early in the timeline as you apply the methodology. You can also reflect on the lessons learned and think about how you could have avoided some of the challenges that occurred on the project by using a more structured change management approach.

© Prosci, Inc. All rights reserved

Prosci Change Management

Project Profile

During the program, you are expected to apply the Prosci Methodology and tools on a project that is currently underway or planned in your organization. The quality of your learning experience depends on having a well-defined project. Please refer to the Project Selection FAQ for guidance. If you don't have all the details required to answer the following questions, seek help from your sponsor, project team members and other colleagues. Your instructor will review your project summary prior to the delivery of the program.

1. Name

2. Email

3. What is the name of your project?

4. Is anyone else in this class working with you on this project?

- ○ Yes
- ◉ No

5. Please provide the names of the other program participants working on the project:

6. Provide a description of the project, including the nature and scope of the change.

© Prosci, Inc. All rights reserved

7. What are the project objectives? (What is the project intended to achieve?)

8. What project management approach is being used on the project?

- ○ **Sequential** – the project is being executed using a sequential approach that concludes with an implementation phase; e.g. waterfall approach
- ◉ **Iterative** – the project is being executed in smaller phases (also known as cycles); e.g. agile approach
- ○ **Hybrid** – the project is being executed using a combination of sequential and iterative approaches
- ○ **Unsure** – the project management approach has not been decided or is not known at this time

© Prosci, Inc. All rights reserved

PCT Assessment

Assessing Project Health

Prosci®

PEOPLE. CHANGE. RESULTS.™

PCT Assessment

The Prosci Change Triangle (PCT) Model is a simple but powerful framework for understanding the four critical aspects of any successful change effort:

- **Success:** clarity on the aim or purpose of the initiative.
- **Leadership/sponsorship:** provides strategy, direction and guidance.
- **Project management:** addresses the technical side of change by designing, developing and delivering the solution.
- **Change management:** addresses the people side of change by enabling people to engage, adopt and use the solution to achieve results and outcomes.

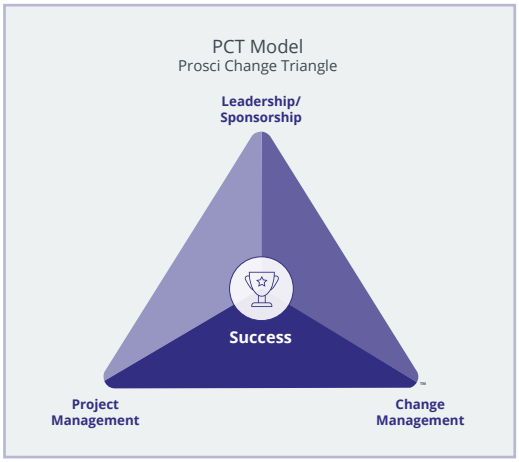

Why:

The PCT Assessment is used to position the project for success by assessing project health across the four critical aspects at a point in time. If a project is weak in any of the four elements, it will struggle or fail. PCT Assessment scores are a leading indicator of the potential for a successful implementation.

The PCT Model is valuable for project teams and change management professionals in a number of ways:

- Provides project teams with common language and context for the four elements of successful change.
- Positions the unique contribution of change management relative to project management and leadership/sponsorship.
- Evaluates the health of an initiative at a point in time. Through repeated application, it evaluates progress over the project lifecycle.
- Identifies organizational competencies and gaps by looking at assessment results from multiple projects.

When:

Complete an initial PCT Assessment early in the lifecycle of the project to establish a baseline. Conduct the assessment again at key points during the project to see if scores are improving. Each time the assessment is conducted, create a set of action plans to improve performance where scores are low.

Who:

The PCT Assessment can be completed by the change management team, project team, senior leaders and key business leaders from the impacted groups.

PCT Assessment

Rank each factor on a 1-3 scale: 1 = inadequate, 2 = adequate, 3 = exceptional

Success	Score: 1–3
1. Inputs into the change management process are defined (may include a business case, charter, scope, or plan).	
2. Organizational benefits are fully defined (what the organization gains).	
3. Project objectives are fully defined (what the project achieves).	
4. Adoption and usage objectives are fully defined.	
5. Units of measure for benefits and objectives are established.	
6. Benefits and objectives are prioritized.	
7. Benefit and objective ownership is designated.	
8. People dependency of benefits and objectives is evaluated.	
9. The definition of success is clear and ready to be communicated.	
10. The sponsorship coalition is aligned to a common definition of success.	
Sum of points for Success (out of 30 total)	0

Leadership/Sponsorship	Score: 1–3
1. The change has a primary sponsor with the necessary authority over the people, processes and systems to authorize and fund the change.	
2. The primary sponsor can clearly explain the nature of the change, the reason for the change, and the benefits for the organization.	
3. The organization has a clearly defined vision and strategy.	
4. The change is aligned with the strategy and vision for the organization.	
5. Priorities are set and communicated regarding the change and other competing priorities.	
6. The primary sponsor is resolving issues and making decisions related to the project schedule, scope and resources.	
7. The primary sponsor is actively and visibly participating throughout the lifecycle of the change.	
8. The primary sponsor is encouraging senior leaders to participate in and support the change by building a sponsor coalition.	
9. The primary sponsor is building awareness of the need for the change directly with employees.	
10. The primary sponsor is visibly reinforcing the change by celebrating successes and addressing resistance.	
Sum of points for Leadership/Sponsorship (out of 30 total)	0

Project Management	Score: 1–3
1. The nature of the change is clearly defined including who is impacted and how.	
2. The project has specific objectives.	
3. The project has a clearly defined scope.	
4. The project has a project manager assigned to manage the project lifecycle.	
5. Project milestones are identified and a project schedule is complete.	
6. A work breakdown structure with deliverables is complete.	
7. Resources for the project are identified and acquired.	
8. Periodic meetings are scheduled with the project team and key stakeholders to track progress and resolve issues.	
9. The project manager understands the value of change management in ensuring the change will be adopted and used.	
10. The Change Management Plan is integrated with the Project Management Plan.	
Sum of points for Project Management (out of 30 total)	0

Change Management	Score: 1–3
1. The change is applying a structured change management approach to deliver the benefits to the organization.	
2. An assessment of the change and its impact on individuals and the organization is complete.	
3. An assessment of the change risk is complete.	
4. The change has specific adoption and usage objectives.	
5. An assessment of the strength of the sponsor coalition is complete.	
6. A customized and scaled change management strategy with the necessary sponsorship commitment is complete.	
7. The resources required to execute the change strategy and plans are identified, acquired and prepared.	
8. Change management plans that will mitigate resistance and achieve adoption and usage are complete and are being implemented.	
9. The effectiveness of change management is being monitored and adaptive actions are being taken if required to achieve adoption and usage.	
10. The organization is prepared to own and sustain the change.	
Sum of points for Change Management (out of 30 total)	0

PCT Assessment Analysis

PCT Profile:

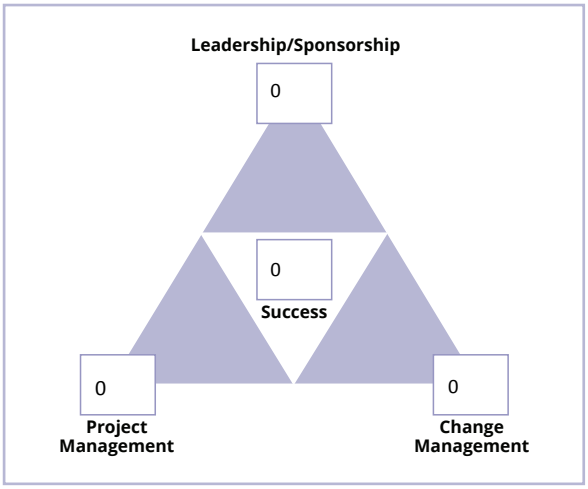

Score interpretation:

10-19	High risk/threat – needs immediate action
20-24	Alert/possible risk – needs further investigation
25-30	Strength – should be leveraged and maintained

Notes

Actions to Improve Project Health

What specific factors need to be addressed to improve project health?

Aspect: (S, L/S, PM, CM)	Factor #	Action

Date of next PCT Assessment:	

Not intended for further distribution.
Prosci and PCT image are registered trademarks of Prosci Inc.
© Prosci Inc. All rights reserved.
